

**Automist Installation Company Ltd**

Unit 1, Industrial Estate,  
Clapham Way,  
Kent SE9 4PQ,  
London, United Kingdom

## AUTOMIST INSTALLATION AND COMMISSIONING CERTIFICATE #SAMPLE

**Installation Date** 2019-03-28 **Installation Engineer** John C **Installer Reference** 3THRH

**Installation Address** 12 Kensington Rd, Sidcup, Kent DA6 4AL, United Kingdom

### Installation Details

Pump Location	Serial	Head Type	Pressure (bar)	Electrical Connection
Under Stairs	0156712	WSS - Wall Smartscan (03330)	95	Circuit #1 (C16 Dedicated)

**Electrical Notes** The installation consists of 1 circuit(s) using FP200 cable with a single pump on an independent electrical supply.

**Activation Kit** Heat alarm(s) with sealed ten year lithium battery.

**Purpose of Installation** **Compliance with** Building Regulations (AI)  
**Approval authority** N.A (Building control surveyors ltd)

**Notes and Deviations** This form certifies that the Automist unit(s) detailed above were successfully commissioned on 2019-06-28. The installer has attested that the equipment has been correctly installed and tested. Any deviations from guidance or best practice are mentioned in *italics* below.


***Automist unit(s) may be connected to detectors with battery power only. System must be serviced annually. The electrical and water supplies and cabling/power for detection were installed by the customer's contractor(s).***









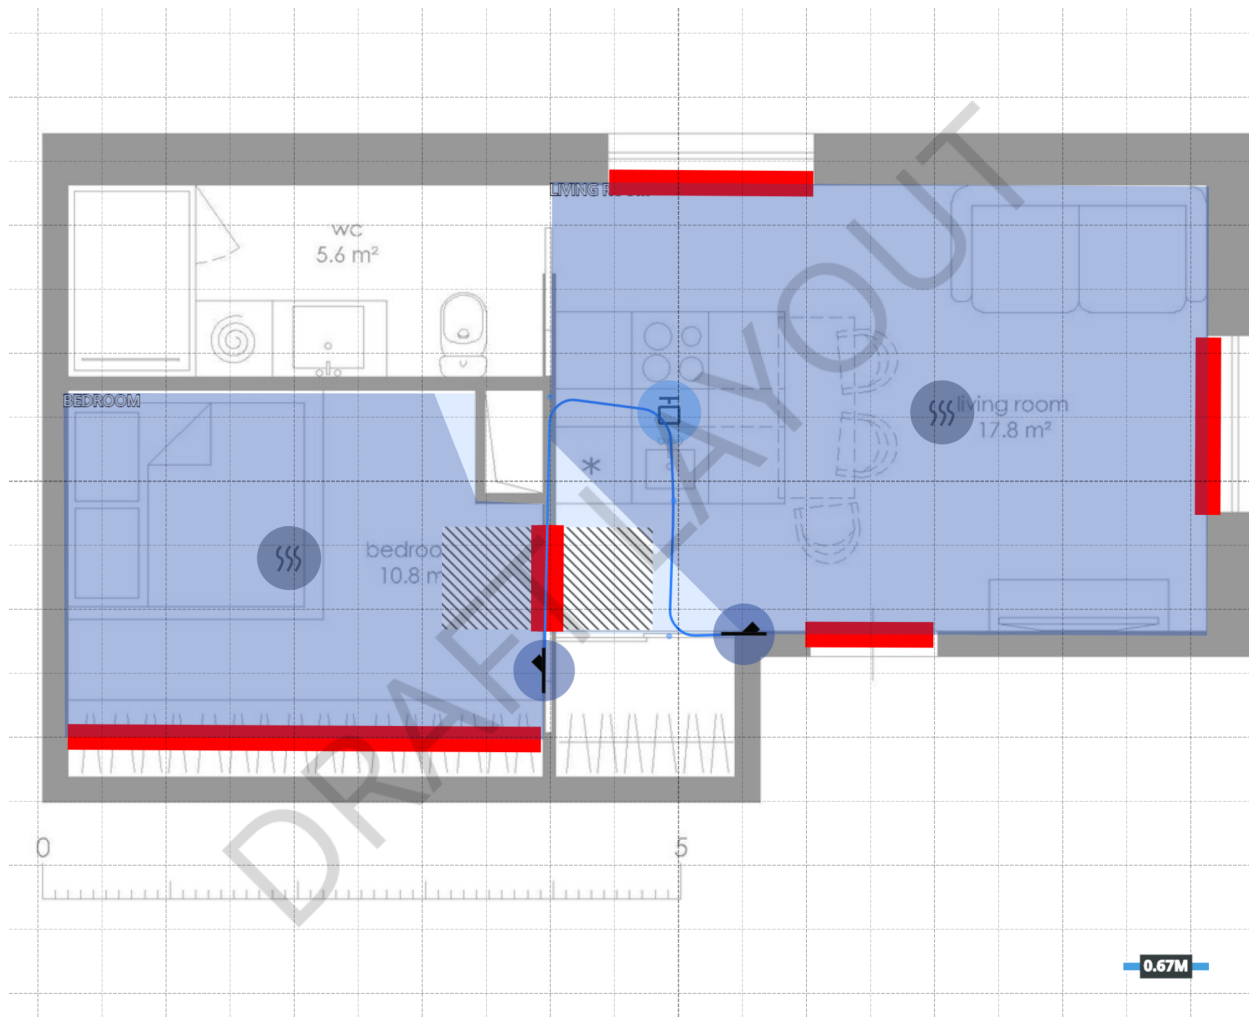


### Service Details

**Service Contact** Automist Installation Company Ltd

**Email** info@plumis.co.uk **Telephone** 0207 555 1234

**Serviced On** 2019-03-28 **Service Due** 2020-03-28



Company	Email	Pump Coverage	Key
	Not specified	25.75M <sup>2</sup>	 Smartscan
	<b>Address</b>	<b>Unprotected Area</b>	 Detectors
	12 Kensington Rd Sidcup Kent DA6 4AL United Kingdom	0.70M <sup>2</sup>	 Pump
	<b>Date</b>	<b>Inventory</b>	 Unprot. Area
	30/06/2019	2 Smartscan sprayhead	 Door
	<b>Reference</b>	0 Fixed head sprayhead	 Hob
	Sample 0.1.1	1 Pumps	 Fire Hazard
<b>Notes</b>		1 (7.56M) Hose 1/4"	 Controller
Objective: Full coverage		0 (0M) Hose 5/16"	 Worktop
Coverage in all areas except bathrooms under 5 sqm & rooms below 1m wide		0 (0M) Wire	 Window
		0 Controllers	
		2 Detectors	
